



TABLE OF CONTENTS

1	ABO	UT US	3			
Z	PROJ	OJECT SCOPE4				
	2.1	Problem Description	4			
	2.2	Assumptions	4			
3		KK BREAK DOWN STRUCTURE AND EFFORT ESTIMATE				
4	PROJECT DEVELOPMENT METHODOLOGY - SCRUM					
5	Proj	PROJECT EXECUTION STRATEGY				
6	Pric	PRICING STRUCTURE				



1 About Us

Frigate India private limited is a multi-skilled software service provider with a highly competent workforce. With years of honed expertise in cross-platform skills and quality-integrated methodologies, we adopt a competent global delivery model in providing value-based solutions as well as professional services to clients worldwide. Our strongest advantage is the excellent pool of skilled resources, recruited from the finest clan of professionals in the industry.



2 Project Scope

2.1 Problem Description

Edujuice had approached application targeting the mobile phones. The purpose of the application social networking application for educators students and businesses for non interactive videos and interactive classes on video... It's a social networking application for educators(teachers) and academies (eg. ISB.. Time Coaching)* and students for non_ interactive videos and interactive classes on videocall.

2.2 Assumptions

- Edujuice will provide relevant information that would help achieve the objectives of this project
- All the APIs required for the functionality will be provided by Edujuice
- If any significant changes occur in the requirements or if there are any additional deliverables that are required, Frigate and Edujuice will add a mutually agreed cost based on the changes in the requirement.
- Review iterations/revisions will be as per what is indicated in Frigate Project Plan. Any subsequent iteration, beyond those reasonably required will have to be indicated by Frigate at the start of the project and it may cause an impact on schedule and cost.
- Any information request, feedback, clarification and sign-offs shall be addressed within 2 business days during the project cycle.
- Frigate extends continuous support and co-ordination during the execution of the project.
- Frigate would nominate single point of contact for the engagement. This person will have a detailed understanding of the Project requirements. He/ She should have access to all the



individuals and information related to the engagement in order to provide the Frigate team members with the necessary information whenever needed.

- Frigate shall commence work only on receipt of a valid Purchase Order.
- All the common modules will be packaged so that they can be reused.
- MVC design architecture is followed
- Frigate will checking in/out the code to the Frigate Bitbucket repository and ensure to follow the best coding standards and structure
- Frigate will be releasing working builds in regular intervals as per the project development plan
- Frigate will support Edujuice extensively when the application moves to production environment
- Frigate will provide Project Knowledge Transfer to Edujuice after completion of the project



3 Work Break down Structure and Effort Estimate


		No. of
S. No	Features	hours
1	Project Setup	8
	Registration/Sign up with user Facebook/email	
	(Students / Professionals / Job seekers /	
2	Enterprises/Advertisers / News publishers)	50
	Login user with Facebook/email (Maintain different	
3	roles and display screens based login user)	30
	Students:	
	Create own profile to showcase his projects and	
4	career	40
	Follow the other users/advertisers/news publishers	
5	etc. in our platform	80
	Ability to view all course based on favorite	00
	enterprises, advertisers, news publishers,	
6	professionals etc. (Main Stream of content)	120
7	Students can create his own story or content	50
	Sharing our content to other social sites Like: FB,	
7	Twitter etc.	16
	Add courses in to his profile cart to buy.	8
8	Ability to view trail course/period	20
9	Payment gateway (Pay pal, CC, DEBIT, Apple pay)	50
	Professionals:	
	Create own stories Or search existing	
10	content/courses in our platform	40
	Ability to view all course based on favorite	
	enterprises, advertisers, news publishers,	
	professionals etc. (Main Stream of content) (If its	4.0
11	same structure for all users hours may be differed)	10
12	Testing	60
13	Project Management	30
	Total	612



4 Project Development Methodology - SCRUM

Frigate utilizes several methodologies such as: Agile, SCRUM and Waterfall. Frigate has chosen to use SCRUM methodology for this project.



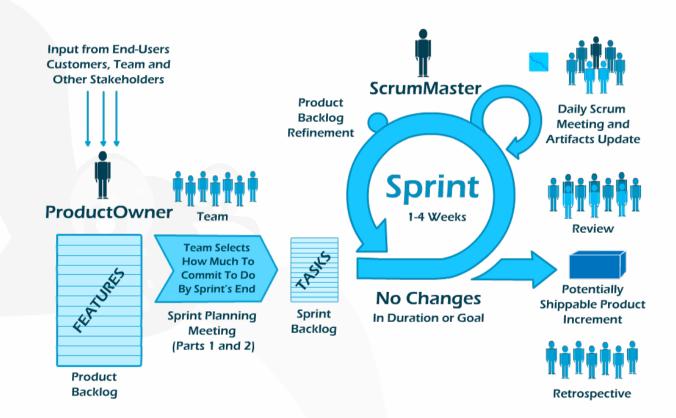



Project Execution Strategy

Location

Frigate proposes that the project will be executed on a fixed bid basis.

Execution Methodolog Frigate proposes to follow agile development / SCRUM model for the project execution.

y

Project

Frigate will designate a Project Manager, who will be **Management** responsible for project delivery.

- Project Manager will coordinate all the conference calls between the Frigate team and Edujuice.
- The Project Manager will be monitoring and tracking progress of the tasks against Edujuice approved schedule.
- The Project Manager will be the first escalation point for Edujuice-The Project Management and Management shall be reflected upon in Daily updates.

Quality Assurance

- Frigate proposes to use peer reviews for QA purposes
- All standards, templates and procedures will be documented.
- All deliverables will be verified against the standards, templates and project procedures of Edujuice.
- All issues reported during the reviews will be closed after due corrective action.

Communicat ion

• All communications with Frigate will be through emails, phone calls and check-point meetings.

Status Reporting

- Frigate team will submit weekly status report by COB Friday, with status review on Monday as agreed by Frigate and Edujuice.
- Frigate proposes to use following template for status report.





Issue Tracking Issues related to development and testing will be maintained in any tool as agreed upon by Edujuice and Frigate.

Change Management This proposal is based on the assumption that the scope of the project will not change after the requirements and design are signed off. If there is any change to the scope / requirements / design after the sign off, all such changes need to the routed through the following change management process:

- Initiating a change request
- Impact assessment and estimate in terms of project time line and cost
- Review and approval of change request by Edujuice project coordinator
- Applying changes to schedules and PO
- It is assumed that all reviews will be completed and approvals will be provided by Edujuice in 2 business days from the date of receipt of the deliverable by Edujuice project coordinator and the schedules will be developed with this assumption. Any delay beyond 2 business days would impact the time line and project cost. It would follow the above change management process.

Escalation

Narayana Reddy Marudi, Chief Operating Officer

Point of

of email: mnreddy53@gmail.com

Contact

Deployment

Plan

Frigate will provide a deployment plan to Edujuice during the design stage. Frigate will test the functionality before deployment.



6 Pricing structure

Total Hours	612 hours
Total Cost (15 \$ per hour)	\$ 9,180
